

I-75 Modernization Project, Oakland County

North of 13 Mile to South Boulevard

July 30, 2020

www.Modernize75.com | (313) 518-1078



Job Number: 201437 | CS 63174
 Contractor: Walsh/Toebe Joint Venture
 For additional historical info visit:

Michigan.gov > [MDOT](#) > [I-75 Modernization Project](#)

SEGMENT ONE (Opened to traffic in 2017)
 North of Coolidge to North of South Boulevard

SEGMENT TWO (Under Construction)
 North of 13 Mile to North of Coolidge Hwy

VIDEOS




Project Corridor



Big Beaver Diverging Diamond Interchange

PHOTOS

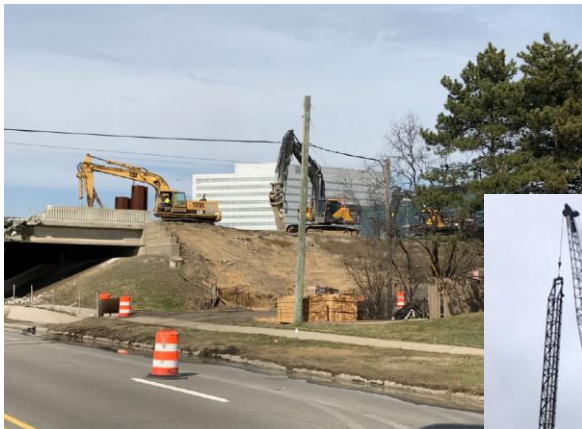

Livernois Bridge Demolition



Lifting Pile at Big Beaver

[View photo gallery](#)

SEGMENT TWO

North of 13 Mile to North of Coolidge Hwy

Northbound I-75 exit to Big Beaver **facebook**

Road to close on Tuesday

POSTED JUL 27 2020

Weather permitting, crews will be closing the northbound I-75 exit to Big Beaver Road for interchange construction starting Tuesday, July 28th at

Construction Progress to Date

87%

PHONE CALLS (Started November 21, 2018)

128 calls asking for directions

65 calls asking about project timing

70 calls with project concerns

187 calls asking for project info

PRESS RELEASES

Michigan.gov > [Press Releases](#)


Modernize75.com > [Press Releases](#)

SOCIAL MEDIA

<https://www.facebook.com/modernize75>

<https://twitter.com/Modernize75>

SCHEDULE

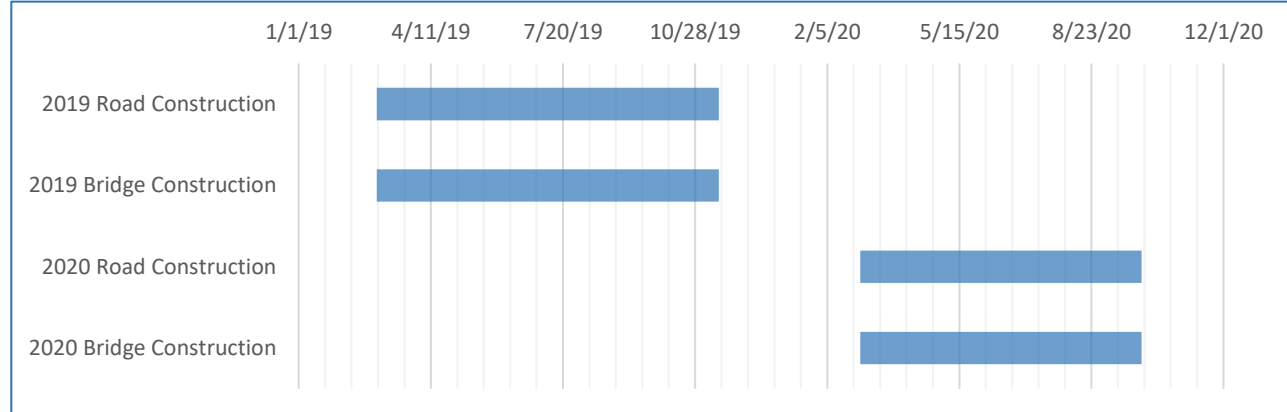

COSTS



Original Contract	\$223,431,500
Contract Changes	\$17,748,293
Total Current Contract	\$241,179,793
Paid to Date	\$209,929,236
Contract Bal Remaining	\$31,250,557
Percent Complete	87%
