

I-75 Modernization Project, Oakland County

M-102 to South Boulevard

May, 2019

www.Modernize75.com | (313) 518-1078



Job Number: 201437 | CS 63174
 Contractor: Walsh/Toebe Joint Venture
 For additional historical info visit:

Michigan.gov > [MDOT](#) > [I-75 Modernization Project](#)

SEGMENT ONE (Opened to traffic in 2017)
 North of Coolidge to North of South Boulevard

SEGMENT TWO (Under Construction)
 North of 13 Mile to North of Coolidge Hwy

SEGMENT THREE
 North of M-102 to North of 13 Mile Road

VIDEOS



Project Corridor



Square Lake Interchange Traffic Plan

PHOTOS



Big Beaver Rd. Bridge Demo



Crooks Rd/Corporate Dr. Bridge Demo

[View photo gallery](#)

SEGMENT TWO

North of 13 Mile to North of Coolidge Hwy

05.08.19

Bridge demo to close the I-75 Freeway from I-696 to Square Lake Road

Starting Friday, May 10th at 10pm, crews will be closing both directions of I-75 for bridge demolition at Wattles and Crooks/Corporate. Since these bridges are over the freeway, it is not safe to do this work with freeway traffic moving underneath. At the time of the closing, roadway pavement repairs will also occur. We will completely close the freeway and ramps from I-696 to Square Lake until 5am on Monday, May 13th.

...

CONSTRUCTION PROGRESS TO DATE



facebook

Comments on 4/29/2019 update:

Kathleen T. – Love the pics! Nice job on the clean up! Big beaver looked great with no evidence of such a big demolition!

John B. – Love the Progress Reports! Keep it up!

PHONE CALLS (Started November 21, 2018)

- 74 calls asking for directions
- 24 calls asking about project timing
- 20 calls with project concerns
- 48 calls asking for project info


PRESS RELEASES

- Michigan.gov > [Press Releases](#)
- Modernize75.com > [Press Releases](#)


SOCIAL MEDIA

- <https://www.facebook.com/modernize75>
- <https://twitter.com/Modernize75>

SCHEDULE

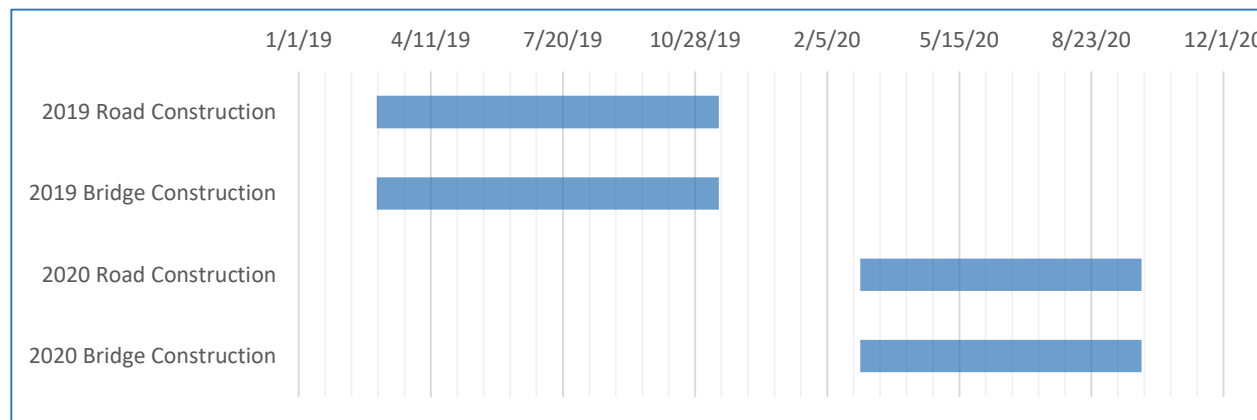

COSTS

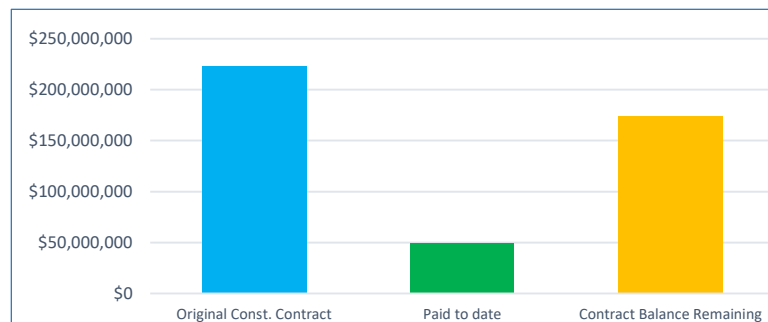

Original Contract	\$223,431,500
Contract Changes	\$903,386
Total Current Contract	\$224,334,886
Paid to Date	\$49,528,110
Contract Bal Remaining	\$174,806,776
Percent Complete	22%
